

Test Report Ref: TR 731047


**RESULTS CONTINUED:**

**Laboratory Dry Density & Water Content Test Result**

Maximum Dry Density	1.91 Mg/m <sup>3</sup>
Optimum Water Content	12 %
Actual Dry Density	1.91 Mg/m <sup>3</sup>
Actual Water Content	12.2 %

**Particle Size Distribution Test Result**

BS Test Sieve Nominal Aperture	As Received Test Portion % Passing	Stable Test Portion % Passing
63.0 mm	100	100
40.0 mm	94	100
31.5 mm	91	97
16.0 mm	72	77
8.0 mm	55	63
4.0 mm	37	49
2.0 mm	24	39
1.0 mm	18	32
0.063 mm	3.6	9.9

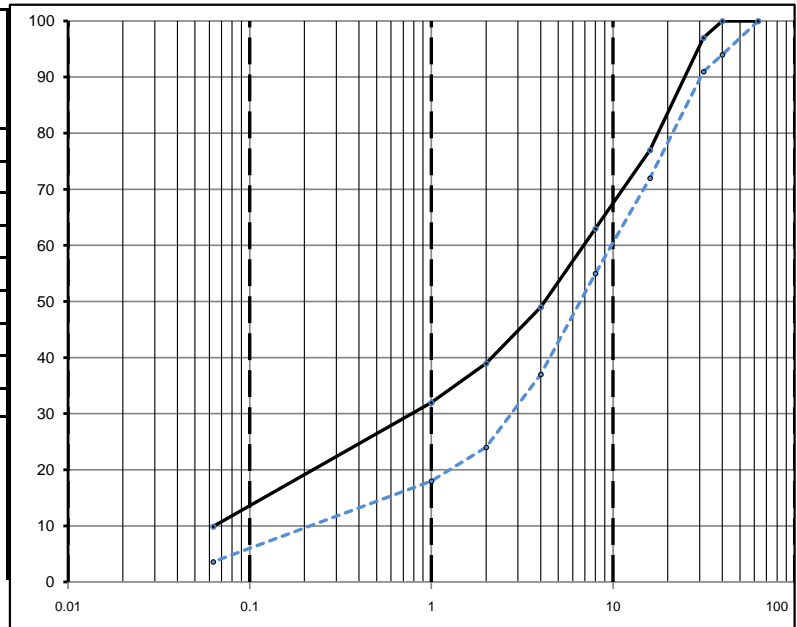

This test report shall not be reproduced, except in full, without the written approval of Celtest Company Limited.

These results relate only to the items tested.

**Comments:**

None

Report checked and approved by:

Mathew Sayer  
Aggregate Team Manager
